



Hunters Point Naval Shipyard Parcel G Building Demolition Progress Update



Week of: July 06, 2026

Achievements

- Building 351 – Continue with disposal of demolition debris. Small amount remains.
 - Soil Tackifier applied on Thursday, 09-July.
- Building 401 – Demolition Started on Monday (06-July-2026)
- Building 439 – Abatement completed

Upcoming Work Week: July 13, 2026

- Building 401 – Disposal of material, start demolition of foundation
- Building 351 – Continue with disposal of remaining demolition debris



Bldg 401 – Thursday, 09-July-2026: 95% demolished. Concrete Slab still in place.



Bldg 401 - Monday start of the day (06-July-2026)




Hunters Point Naval Shipyard Parcel G Building Demolition Progress Update



Bldg 351: 06-July-2026: 99.9 % of debris removed

Soil Tackifier applied on Thursday, 09-July.

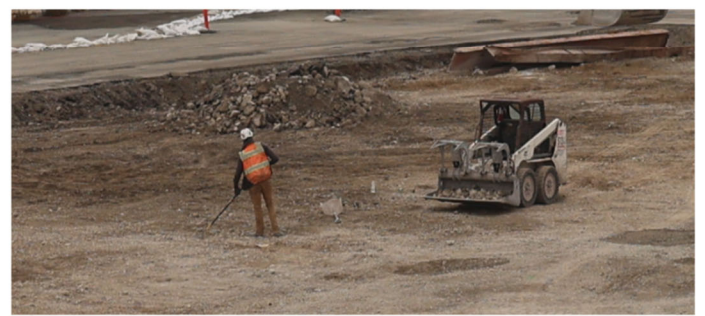

401

366

351

351A

411

439

408 slab

Project Overview:

The Navy is demolishing six buildings and one former building slab at Parcel G under a Multiple Award Construction Contract. This work is the one of the final steps in the environmental cleanup activities at Parcel G in preparation for property transfer to the City and County of San Francisco.
